

EVENT ORGANISATION AND REPLICATION MANUAL

PRACTICAL GUIDE FOR FAMILY-CENTERED SPORT EVENTS

ERASMUS-SPORT-2025-SNCESE
101245417
Home & Heart European Family Festival
September, 2026
Riga, Latvia

About this manual

The Home & Heart Event Organisation and Replication Manual is a practical guide for municipalities, sport federations, sport clubs, community organisations and project partners that want to organise a family-focused sport festival inspired by the Home & Heart model. It translates the project experience into a reusable event methodology covering planning, coordination, participant recruitment, programme design, inclusion, safety, communication, digital engagement, monitoring and long-term continuation.

The structure draws on two practical sources supplied for the project: the earlier Manual for Organisation of the BeActive Beach Games and the Event Organization Guideline checklist. The manual does not copy those sources mechanically; it adapts their planning logic to the Home & Heart model and to the lessons from the 2026 implementation in Riga.



Examples of Home & Heart Family Cup activities used as practical reference material.

Pilot element	Riga 2026 reference
Public festival	19 September 2026, Uzvaras Park, Riga; free participation; 11:00-17:00.
Public engagement	657 families and 2,320 participants.
International Family Cup	50 family teams / approximately 200 active participants.
Structured competition	12 Family Cup activity stations with live results and standings.
Digital legacy	Livestream, educational content, practical guides and resources available through the Digital Knowledge Hub.

How to use the manual

Sections 1-15 explain the event model and organisational process. The appendices reproduce the operational checklist framework as practical templates that can be copied into a local event plan and assigned to named owners.

Contents

1. Introduction and purpose	4
2. The Home & Heart festival model	4
3. Core principles for replication.....	5
4. Planning timeline and workstreams.....	6
5. Governance, roles and partner responsibilities.....	7
6. Participant recruitment and family journey	8
6.1 Define the target groups.....	8
6.2 Recruitment channels.....	8
6.3 Participant journey.....	8
7. Venue, infrastructure and accessibility.....	10
Accessibility approach.....	11
8. Programme design and public activity zone.....	12
9. Family Cup model and station design	13
10. Safety, safeguarding, permits and data protection	15
11. Weather and contingency planning.....	15
12. Volunteers, staffing and partner coordination.....	16
13. Communication and digital engagement.....	17
14. Sustainability, budget, monitoring and post-event follow-up.....	18
14.1 Sustainability and inclusion	18
14.2 Budget and procurement.....	18
14.3 Monitoring and evaluation.....	18
14.4 Post-event wrap-up.....	18
15. Riga 2026 implementation example and lessons learned	20
Practical lessons.....	21
Appendix A. Complete Home & Heart organisation checklist templates.....	22
A1. Event profile.....	23
A2. Roles and responsibilities.....	24
A3. Key milestones.....	26
A4. Permits, compliance and safety	27
A5. Venue and infrastructure register	28
A6. Programme schedule.....	30
A7. Participant journey.....	31
A8. Communications and promotion.....	32
A9. Volunteers and staffing.....	33
A10. Budget and suppliers.....	34
A11. Sustainability and inclusion.....	35
A12. Data collection and reporting.....	36
A13. Risks and mitigation	37
A14. Lessons learned and recommendations	38

1. Introduction and purpose

Home & Heart is designed as more than a one-day sports event. It is a family-centred participation model in which children and adults discover physical activity together, interact with sport organisations, learn practical health and safety messages, and build positive shared experiences.

The manual provides a step-by-step framework that can be adapted to different countries, municipalities, venues and event sizes. It is deliberately flexible: a local organiser may implement a compact family activity day with a small number of stations, while a larger organiser may combine an open public festival, a structured Family Cup, a stage programme, educational content and digital participation.

Replication principle

Keep the core values - family participation, inclusion, cooperation, varied physical activity, learning, safe delivery and long-term access to resources - while adapting the scale and detailed programme to the local context.

2. The Home & Heart festival model



Model component	Purpose	Typical implementation
Open public festival	Low-threshold access to many forms of sport and movement.	Free try-out stations, demonstrations, workshops, activity cards and family-friendly side programme.
Family Cup	Structured teamwork and measurable family participation.	A common circuit of family challenges with timing/scoring, standings and a final.
Educational programme	Practical knowledge that supports healthier family habits.	Short expert sessions, interviews, quizzes and activity-based learning.
Inclusion and support	Reduce barriers to participation.	Free access, adapted tasks, clear information, targeted recruitment and support staff.
Digital engagement	Extend the event beyond the venue and date.	Livestreams, videos, guides, interactive tools and the Digital Knowledge Hub.
Replication and legacy	Allow other organisations to use the model.	Manuals, templates, activity instructions, case studies and reusable digital resources.

The wider festival should prioritise participation and discovery rather than elite performance. Competition can be motivating, especially in the Family Cup, but families should also have non-competitive ways to participate, learn and enjoy movement together.

3. Core principles for replication



Family first: Design the event around adults and children taking part together, rather than creating separate parallel experiences.

Sport for all: Choose activities that can be tried without previous sport experience and that can be adjusted to different ages and abilities.

Cooperation and communication: Include tasks that require family members to coordinate, communicate, solve problems and support each other.

Choice and flexibility: Allow families to choose activities, move at their own pace and take breaks; avoid forcing one fixed route on all visitors.

Inclusion by design: Consider mobility, language, cost, confidence, disability and family circumstances during planning rather than treating accessibility as an afterthought.

Learning through participation: Use sport and play to communicate practical messages about health, safety, nutrition, inclusion and everyday movement.

Digital continuity: Preserve useful content online so that families and organisations can continue using the project materials after the event.

Local adaptation: Retain the core concept while adapting activities, partners, venue and communication to local needs and resources.

4. Planning timeline and workstreams

FIVE-STAGE ORGANISATION CYCLE



For a large multi-partner family festival, planning should normally start around 9-12 months before the event. The exact lead time depends on venue permissions, procurement, international participation, temporary infrastructure and the scale of the public programme.

Timing	Priority actions	Outputs
T-12 to T-9 months	Define concept, objectives, scale and target groups; identify date/venue options; establish core team; draft budget.	Concept note, draft budget, preliminary responsibility matrix, preferred date and venue.
T-9 to T-6 months	Secure venue; engage municipality and sport partners; map permits; define activity formats; establish risk register.	Venue confirmation, partner list, permit plan, draft programme, initial risk register.
T-6 to T-3 months	Open recruitment; contract suppliers; confirm activity providers; develop registration, accessibility and digital plans.	Registration system, supplier list/contracts, activity list, staffing and communication plan.
T-3 to T-1 month	Finalise programme, site map, logistics, equipment, volunteers, medical/safety arrangements and participant information.	Final programme, technical map, contact list, volunteer schedule, emergency procedures.
Final 2 weeks	Confirm participants and suppliers; check weather; brief all parties; test systems; prepare materials.	Final operational pack and go/no-go decision procedure.
Event day	Operate registration, activities, stage, support points, safety, media and data collection.	Delivered event and implementation evidence.
T+1 day to T+2 weeks	Thank stakeholders; publish content; analyse participation; collect feedback; close operational issues; hold debrief.	Evaluation, lessons learned, data summary and follow-up actions.

Minimum critical documents

Event concept; responsibility matrix; milestone plan; budget; venue/site plan; programme; participant journey; risk register; emergency contacts; weather contingency plan; supplier register; communication plan; volunteer plan; accessibility checklist; data and evaluation plan.

5. Governance, roles and partner responsibilities

One organisation should hold overall responsibility, while each workstream has one clearly identified owner. Supporters and suppliers may assist delivery, but accountability should remain explicit. The uploaded checklist is useful here because it links each workstream to an owner, dependencies, deadlines, priority and status.

Workstream	Lead responsibility	Typical support
Overall coordination	Event director / project coordinator	Core organising team, municipality, venue
Venue and technical setup	Technical manager	Event supplier, venue operator, activity providers
Sport and activity programme	Programme lead	Sport federations, clubs, coaches, instructors
Family Cup	Competition lead	Station supervisors, results team, volunteers
Registration and participant data	Registration/data lead	IT support, partner organisations
International families	Participant logistics lead	Associated partners, travel/accommodation providers
Safety and medical	Safety lead	Medical provider, security and public services where required
Accessibility and inclusion	Inclusion focal point	Venue, volunteers, activity providers
Communication and media	Communication lead	Partners, photographer/video team, media contacts
Livestream and digital	Digital lead	AV supplier, content team, Knowledge Hub team
Volunteers	Volunteer coordinator	Team leaders and workstream owners
Finance and procurement	Financial/administrative lead	Project manager, suppliers
Monitoring and evaluation	Reporting lead	Registration team, survey/data support, partners

6. Participant recruitment and family journey



6.1 Define the target groups

The Home & Heart approach is designed for families across generations and should actively include people who may have fewer opportunities to participate in organised sport. Depending on local priorities, targeted groups may include families with low sport participation, low-income families, single-parent families, migrant or recently relocated families, people with disabilities and other groups identified together with local partners.

6.2 Recruitment channels

- Partner organisations and sport federations
- Municipalities, schools, youth centres and family organisations
- Social services, NGOs and organisations working with vulnerable groups
- Sport clubs and community associations
- Event website, social media and newsletters
- Local media and partner communication channels
- On-site registration where capacity and safety arrangements allow it

6.3 Participant journey

Stage	What should happen	Main tools
Registration opens	Use a simple form and collect only information necessary for delivery and reporting.	Online form, privacy notice, confirmation email
Pre-event communication	Send programme, location, arrival instructions, accessibility contact and weather updates.	Email, website, FAQ, map
Arrival	Make the entrance, registration and information points easy to identify.	Signage, volunteers, queue plan
Check-in	Confirm participation and distribute activity cards or other materials.	Participant list, cards, identifiers
Participation	Families choose public activities or follow their Family Cup schedule.	Map, activity card, station staff
Support	Keep information, medical and accessibility assistance visible throughout.	Info point, medical point, contact list
Feedback	Collect short feedback while the experience is still fresh.	QR survey, staff prompts

Stage	What should happen	Main tools
Follow-up	Share photos, results, learning resources and further activity ideas.	Email, social media, Digital Knowledge Hub

THE FAMILY JOURNEY



7. Venue, infrastructure and accessibility



Example of the Home & Heart festival territory concept used during venue planning.

The venue should support safe movement between activities, visible support points and flexible family participation. Existing public infrastructure should be used where possible to reduce cost, but it still needs to be inspected for capacity, accessibility and operational risks.

Zone / requirement	Planning questions
Entrance and registration	Can families find the entrance easily? Is there enough space for queues and activity-card distribution?
Activity zones	Are stations separated enough for safe movement, throwing and queues? Can each provider access equipment/power if required?
Family Cup	Can structured stations operate without interference from general visitor flow?
Stage / demonstrations	Are sightlines, sound, power and technical/backstage areas suitable?
Information and medical	Are support points easy to identify from main visitor routes?
Food and water	Are they separated from active sport zones and supported by waste collection?
Toilets and rest	Are facilities sufficient for the expected audience and usable by people with different mobility needs?
Technical and storage	Is there secure space for equipment and controlled supplier access?
Emergency access	Can emergency services reach key areas without obstruction?

Zone / requirement	Planning questions
Weather protection	What shelter or indoor alternatives exist? What elements must be moved, shortened or cancelled in severe weather?

Accessibility approach

Accessibility should be understood broadly: physical access, clear information, readable signage, flexible participation, reasonable task adaptation, places to rest, access to support staff and inclusive communication. For wheelchair users and people with reduced mobility, review surfaces, gradients, route widths, thresholds and distances between key points. If an activity cannot be made fully accessible, provide meaningful alternative participation rather than excluding the person from the family experience.

8. Programme design and public activity zone

ACTIVITY DESIGN

TRY • DISCOVER • MOVE • LEARN

Mix movement, precision, strategy, education and low-intensity options.



Home & Heart activity examples: basketball challenge, target knockdown, recycling game and moving-spoons teamwork challenge.

A strong Home & Heart programme combines energetic, technical, strategic, educational and lower-intensity activities. The public offer should not depend on one ability or one sport, so that different family members can find something enjoyable and achievable.

Format	Use in a family festival	Examples
Try-out station	Short, low-threshold participation supported by an instructor.	Archery, floorball, table tennis, crossminton
Demonstration	Show unfamiliar sports and invite families to try selected elements.	Kendo, jiu-jitsu, luge training, parasport
Family challenge	A clear task completed together.	Obstacle tasks, precision throws, relays

Format	Use in a family festival	Examples
Mind / precision activity	Alternative to high-intensity movement.	Bridge, darts, novuss, curling
Educational station	Combine activity with practical learning.	Water safety, recycling, healthy habits
Digital / technology activity	Use technology to create interest and measurable challenges.	Virtual cycling, reaction/robot activities
Structured competition	Common route, rules, scoring and standings.	Family Cup
Stage activity	Create shared visibility and energy for the whole venue.	Sport demonstrations, interviews, warm-ups

Public engagement tool

In Riga, each participant received an activity card and collected a mark after completing activities. Families reaching the required minimum became eligible for the prize draw. This simple mechanism encouraged visitors to try several sports rather than only one station.

9. Family Cup model and station design

FAMILY CUP

TEAMWORK MADE MEASURABLE

Structured participation with shared tasks and live results.

50 TEAMS

200 PEOPLE

12 STATIONS




Examples from the 12-station Home & Heart Family Cup, illustrating teamwork, communication, precision and problem-solving.

The Family Cup is the structured competition component of the Home & Heart model. It is designed around cooperation, communication, shared decision-making and varied abilities rather than pure speed or strength.

In the 2026 format, 50 family teams / approximately 200 participants engaged across 12 stations. Eleven stations were family/team activities and one was an individual bonus station. Team stations were primarily ranked by finishing time, with lower overall points producing the better final position.

Station	Main challenge	Family skill emphasised
1. Laser Biathlon	Target shooting and relay movement.	Focus, pacing, shared relay responsibility
2. Ringo Flamingo	Place rings on targets from adapted throwing lines.	Accuracy, strategy, role choice
3. Obstacle Course	Blind participants navigate using verbal guidance.	Trust, communication, listening
4. Ball Path	Coordinate a shared board to move a ball.	Fine coordination, teamwork
5. Basketball Shots	Score in five different hoops.	Accuracy, task-sharing
6. Ball Knockdown	Knock down targets with different balls.	Strategy, accuracy, cooperation
7. Ladder Golf	Reach a target score with bolas.	Precision, role allocation
8. Duck Race	Move a floating duck using air only.	Coordination, patience
9. Cube Puzzle	Assemble a large picture puzzle.	Problem-solving, communication
10. Recycling Game	Sort waste-item tokens correctly.	Learning, teamwork, decision-making
11. Moving Spoons	Transfer a ball through a spoon sequence.	Timing, coordination
12. Blow Challenge	Individual distance challenge with bonus points.	Individual contribution to family result

Station design rule

Each Family Cup station should have a clear objective, standard equipment list, setup instructions, simple rules, measurable result, age/ability adaptation, maximum operating time, safety rule and trained supervisor.



DESIGN THE STATION FOR THE FAMILY

Every task should be simple to explain, safe to run and meaningful to complete together.

1

CLEAR

one objective + one measurable result

2

ADAPTABLE

age / ability adjustments built in

3

COOPERATIVE

roles for more than one family member

4

SAFE

boundaries + supervisor + reset procedure

A station is easier to replicate when its objective, adaptation logic, teamwork role and safety rule are all explicit.

10. Safety, safeguarding, permits and data protection

Safety planning is a core organisational workstream. Requirements depend on the host country and municipality, so organisers must confirm applicable legal and administrative obligations with competent local authorities and professional service providers.

Area	What to confirm
Venue / municipal permissions	Right to use the site, temporary structures, public event permissions and any local conditions.
Medical / first aid	Coverage level, location of medical point, emergency access, incident escalation and documentation.
Security / public order	Security needs, police/fire coordination where required, crowd movement and emergency access.
Child safeguarding	Adult responsibilities, staff conduct, lost-child procedure and supervision principles.
Photo / video	Transparent information about photography and filming and any consent process required.
Data protection	Only necessary data collected; access, retention, participant information and reporting use defined.
Activity-specific safety	Every station provider supplies rules, equipment checks and safe operating boundaries.
Weather	Decision thresholds, monitoring responsibility, communication chain and alternative delivery plan.
Incidents	Single incident log and named person responsible for escalation and follow-up.

For throwing, striking or moving-object activities, active zones should be clearly separated from waiting areas. Participants should enter retrieval or target areas only when the station supervisor confirms it is safe.

11. Weather and contingency planning

WEATHER CONTINGENCY – WHAT RIGA 2026 TAUGHT US



Outdoor family events need a realistic contingency plan that can be activated quickly. The Home & Heart experience demonstrated that weather planning must cover not only the public festival, but also international participants, accommodation, transport, suppliers and already-booked travel.

Contingency question	Recommended preparation
Who decides?	Name the person or group authorised to postpone, relocate, shorten or cancel the event.
What triggers action?	Define weather/safety thresholds and monitoring sources in advance.
When is the decision made?	Set decision points that allow suppliers, participants and authorities to react.
What can move indoors?	Identify programme elements that can continue safely in an indoor venue.
What can be rescheduled?	Pre-agree alternative date options and supplier change conditions where possible.
How are people informed?	Prepare website, email, social and partner-message templates before the event.
What happens to international guests?	Maintain a separate continuity plan for participants who cannot simply return later.
How are costs managed?	Clarify cancellation/change clauses and maintain contingency budget.

Riga 2026 weather lesson

The original public festival date was 22 August 2026. Because of the red weather warning, the public outdoor festival was postponed to 19 September. International families and partners were already in Riga, so their programme was adapted and moved indoors rather than cancelled. Future organisers should therefore separate the public-event contingency plan from the invited/international-participant continuity plan.

12. Volunteers, staffing and partner coordination

Volunteers and partner staff often determine whether a large public event feels clear and welcoming. Recruitment should be followed by role-specific briefing rather than only a general introduction.

Role	Typical responsibilities	Briefing needs
Registration	Check-in, activity cards, participant questions.	Registration system, queues, privacy
Information	Directions, programme questions, lost-and-found support.	Site map, contacts, escalation
Activity support	Queue support, setup/reset, participant guidance.	Station rules and safety boundaries
Family Cup	Timing, result recording, team movement.	Scoring rules, result system, station flow
Stage / AV	Speaker readiness, demonstrations, technical coordination.	Run-of-show, equipment, contact chain
Accessibility support	Assist with directions and practical access needs.	Inclusive communication, routes, escalation
Medical / safety	First response and incident management.	Professional procedures and site layout
Media / content	Photos, video, interviews and live updates.	Shot list, consent/visibility rules, key messages
Clean-up / logistics	Waste, equipment movement and site reset.	Waste plan, technical zones, supplier handover

All operational staff should receive a final event brief containing the site map, programme, responsibility matrix, emergency contacts, weather plan, escalation chain and any participant-specific support information necessary for their role.

13. Communication and digital engagement



Communication has two functions: attracting and preparing participants, and extending the educational and dissemination value of the project. Partners should receive ready-to-use assets so national and local promotion stays consistent while remaining easy to adapt.

Phase	Communication priorities
Before registration	Event concept, date, location, target groups, participation conditions and what families can expect.
Registration campaign	Clear call to action, activity highlights, partner/federation content and accessibility contact.
Final week	Arrival information, map, programme, weather updates, what to bring and any changes.
Event day	Live updates, activity highlights, family stories, results, safety information and schedule changes.
After event	Thank-you message, photos/video, results, participation data, surveys and links to further resources.

Digital Knowledge Hub and livestream

The Digital Knowledge Hub at familyactivityhub.com provides a long-term resource library for families, coaches, sport organisations, municipalities and policymakers, together with practical tools such as the Family Activity Generator. The 2026 livestream also included family interviews and interactive learning on water safety, healthy eating habits, raising healthy athletes, how sport supports children's development and movement as part of everyday life, supported by quizzes on these topics.

Digital Knowledge Hub: <https://familyactivityhub.com/>

Crisis communication

Prepare draft messages for severe weather, programme changes, delays, venue changes and safety incidents before the event. State what changed, why, what participants should do and where the next update will appear.

14. Sustainability, budget, monitoring and post-event follow-up

14.1 Sustainability and inclusion

- Use existing infrastructure where possible.
- Reduce unnecessary single-use materials and printing.
- Provide visible waste collection and sorting.
- Plan responsible catering and water provision.
- Promote public transport, walking and cycling access.
- Protect grass, trees and other sensitive areas during setup and dismantling.
- Keep digital resources accessible after the event.

14.2 Budget and procurement

Cost area	Examples
Venue and permissions	Venue hire, permits and municipal requirements
Technical infrastructure	Tents, stage, sound, power, barriers, furniture
Sport equipment	Station-specific equipment, rental and transport
Participant materials	Activity cards, T-shirts, medals, identifiers
Safety and accessibility	First aid, security, accessibility measures
Communication	Design, printing, advertising, media production
Digital delivery	Livestream, registration/results systems, web services
Travel and accommodation	Invited families, partners and staff where applicable
Food and water	Catering, refreshments and water provision
Staff / volunteers	Subcontracting, volunteer support and briefings
Documentation	Photography, video, reporting and translation
Contingency	Weather changes, replacement equipment and additional logistics

14.3 Monitoring and evaluation

Monitoring should be planned before the event so that participation and engagement can be evidenced rather than reconstructed later. Useful sources include registrations, attendance counts, activity-card completions, Family Cup station results, livestream statistics where available, surveys, media monitoring, incident logs and partner feedback.

For the Family Cup, the live results platform provides especially strong engagement evidence because participation is recorded through station results, points, standings and final qualification rather than attendance alone. For the public festival, activity cards provide a practical indicator of how broadly visitors interacted with the activity offer.


14.4 Post-event wrap-up

- Close supplier handovers, invoices and contractual issues.
- Confirm the venue has been restored and temporary infrastructure removed.
- Thank participants, partners, federations, suppliers, volunteers and supporters.

- Publish results, photos, video and key participation statistics.
- Collect surveys and hold an internal/partner debrief.
- Update the risk register with actual issues and responses.
- Record lessons learned and improvements for the next edition.
- Upload reusable materials to the Digital Knowledge Hub.
- Identify organisations interested in local replication and future funding.

AFTER THE EVENT: TURN DELIVERY INTO LEGACY

A simple follow-up rhythm keeps the festival useful after the final activity closes.

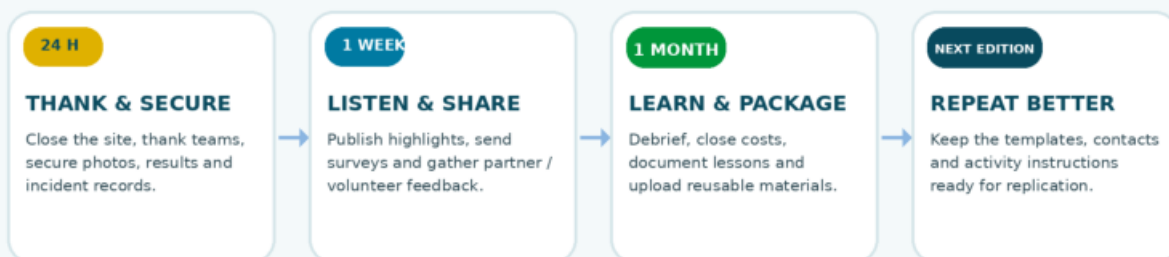

A simple post-event rhythm helps convert a one-day festival into reusable knowledge and future activity.

15. Riga 2026 implementation example and lessons learned

RIGA 2026

A MODEL TESTED IN PRACTICE

Two connected formats:
a structured Family Cup +
an open public festival.

657
FAMILIES

2,320
PUBLIC PARTICIPANTS

50
FAMILY CUP TEAMS

12
CUP STATIONS

LESSON FROM THE PILOT

Plan the public festival and invited-family programme as related, but operationally separate workstreams.



Riga 2026 brought the Home & Heart model together in practice: structured family teamwork, open public participation and a reusable digital legacy.

Element	Riga 2026 example
Public festival	19 September 2026, Uzvaras Park, Riga; 11:00-17:00; free participation.
Public participation	657 families and 2,320 participants.
Public activity offer	A broad programme delivered with Latvian sport federations and partner organisations.
Engagement mechanism	Individual activity cards with marks for completed activities and prize-draw eligibility.
Family Cup	50 family teams / approximately 200 participants; 12 stations; live results and standings.
Digital component	Livestream, interviews, educational sessions, quizzes and post-event access to project materials.
Weather adaptation	Original public date postponed because of severe weather; international programme continued indoors; public festival delivered later.

Practical lessons

1. CENTRAL COORDINATION Use a clear central coordination structure when many sport federations and suppliers work simultaneously.	2. TWO LINKED FORMATS Keep the open public festival and Family Cup linked conceptually but manage them as related operational sub-events.
3. MEASURE PARTICIPATION Use simple engagement tools such as activity cards and live standings to encourage participation and generate measurable data.	4. PREPARE COMMUNICATION Prepare partner-ready communication assets early.
5. PLAN FOR WEATHER Treat weather planning as an operational, communication and financial issue.	6. OFFER VARIED ACTIVITIES Offer activities with different intensity and skill profiles so more family members can participate meaningfully.
7. MAKE LEARNING INTERACTIVE Integrate educational content into interactive formats such as interviews, demonstrations and quizzes.	8. PACKAGE FOR REUSE Prepare reusable outputs during implementation so they can be published quickly in the Digital Knowledge Hub.

Family participation works best when operational clarity and a welcoming event atmosphere are designed together.

Appendix A. Complete Home & Heart organisation checklist templates

APPENDIX A

ORGANISE • ASSIGN TRACK • REVIEW

14 reusable planning worksheets

Use them as a live event-management workbook:

- assign owners
- set deadlines
- record evidence
- capture lessons learned

HOME & HEART ORGANISER TOOLKIT



The following templates are adapted directly from the uploaded Event Organization Guideline workbook. They retain the checklist logic - ownership, deadlines, dependencies, suppliers, status and evidence - while replacing race-specific wording with Home & Heart family-festival terminology where necessary. Organisers can copy the tables into their own workbook or use them as printable planning sheets.

Checklist use

Add rows where needed; be specific about owners and deadlines; mark non-applicable items as N/A rather than deleting them; and use relative timing (for example T-6 months) where the exact event date has not yet been fixed.

A1. Event profile

HOME & HEART ORGANISER WORKSHEET • Complete locally, assign an owner and update as planning progresses.

Item	Local organiser input
Country	
City / region	
Event title	
Event date	
Event type / discipline	
Webpage	
Short overview of the event	
Main goal of the event	
Main target groups	
Short description of main activity / Family Cup format	
Short description of public festival / side programme	
Key expected outcomes	
Specific local conditions to consider	

A2. Roles and responsibilities

HOME & HEART ORGANISER WORKSHEET • Complete locally, assign an owner and update as planning progresses.

Workstream / area	Responsible team	Support / partner	Supplier / stakeholder	Deadline	Status
Overall event coordination					
Venue / site planning					
Permits and local approvals					
Risk assessment and safety					
Medical / first aid					
Registration system					
Participant communication					
Volunteer recruitment					
Volunteer briefing and scheduling					
Equipment and logistics					
Registration / information area setup					
Branding and signage					
Stage / sound / AV					
Programme delivery					
Festival activities / workshops					
Sponsors and partner activations					
Catering / refreshments / water points					
Accessibility and inclusion					
Environmental sustainability					
Family Cup / structured challenges					
Photography / video					
Media / PR / social media					

Workstream / area	Responsible team	Support / partner	Supplier / stakeholder	Deadline	Status
Surveys / participant feedback					
Data collection and reporting					
Post-event wrap-up					

A3. Key milestones

HOME & HEART ORGANISER WORKSHEET • Complete locally, assign an owner and update as planning progresses.

Milestone	Deadline / date	Owner	Dependency	Status	Notes
Event date confirmed					
Venue confirmed					
Event documents finalised (programme, rules, action plan, budget, etc.)					
Permits submitted					
Permits approved					
Suppliers selected					
Registration opens					
Communication campaign starts					
Volunteer recruitment starts					
Training / briefing plan finalised					
Equipment order confirmed					
Final programme approved					
Final risk review completed					
Event team coordination completed					
Event delivered					
Participant reporting completed					
Post-event evaluation completed					

A4. Permits, compliance and safety

HOME & HEART ORGANISER WORKSHEET • Complete locally, assign an owner and update as planning progresses.

Requirement	Needed?	Owner	Deadline	Status	Notes / evidence
Venue permission					
Municipal permit					
Public event approval if required					
Police notification / approval					
Fire department notification / approval					
Medical / first aid coverage					
Insurance					
Child safeguarding arrangements					
Photo / video information or consent process					
Data protection / GDPR arrangements					
Emergency procedures					
Weather contingency plan					
Incident reporting process					
Accessibility / barrier-free access review					

A5. Venue and infrastructure register

HOME & HEART ORGANISER WORKSHEET • Complete locally, assign an owner and update as planning progresses.

Type / item	Details	Qty	Owner / supplier	Delivery / readiness	Notes
Venue name					
Full address					
Main visitor access					
Accessibility by public transport					
Parking availability					
Water access					
Electricity access					
Toilets / sanitary facilities					
Waste management points					
Shelter / indoor backup					
Entrance and registration area					
Family Cup area					
Public festival activity zone					
Stage / demonstration area					
Information / medical point					
Bag storage / staff storage if needed					
Event documentation					
Technical equipment and tools					
Fences / barriers					
Gazebos / tents					
Tables and chairs					
Sound system / microphones					
Stage / screens					

Type / item	Details	Qty	Owner / supplier	Delivery / readiness	Notes
Benches / seating					
Water stations					
Medical station					
Signage					
Flags / banners					
Activity-specific equipment					
Medals / prizes					
Activity cards / participant identifiers					
T-shirts / branded materials					
Recycling bins					

A6. Programme schedule

HOME & HEART ORGANISER WORKSHEET • Complete locally, assign an owner and update as planning progresses.

Time	Activity	Lead person / team	Needed equipment / setup	Notes
Pre-event day	Site handover, move-in and setup			
Event opening	Registration / check-in / activity cards			
Opening	Welcome and orientation			
Morning	Family Cup / public activities / demonstrations			
Midday	Stage programme / educational sessions / interviews			
Afternoon	Festival activities / workshops / try-outs			
Before closing	Prize draw / Family Cup final / awards as relevant			
Closing	Closing announcement			
After closing	Dismantling and site reinstatement			

A7. Participant journey

HOME & HEART ORGANISER WORKSHEET • Complete locally, assign an owner and update as planning progresses.

Stage	What happens	Responsible team	Materials / systems needed	Risks / notes
Registration opens				
Pre-event communication				
Arrival at venue				
Check-in / registration desk				
Activity-card / material distribution				
Opening / orientation				
Family Cup start or public activity participation				
Route / venue support and refreshment points				
Stage / educational engagement				
Prize draw / awards				
Survey / feedback collection				
Departure / follow-up communication				

A8. Communications and promotion

HOME & HEART ORGANISER WORKSHEET • Complete locally, assign an owner and update as planning progresses.

Activity	Channel	Audience	Owner	Start	End	Key message / asset	Notes
Event announcement							
Registration campaign							
Targeted outreach to families							
Volunteer call							
Partner / federation visibility							
Educational-content promotion							
Event-day live coverage							
Media relations							
Weather / change communication							
Post-event thank-you campaign							
Post-event video / photo dissemination							
Promotion of Digital Knowledge Hub / follow-up activities							

A9. Volunteers and staffing

HOME & HEART ORGANISER WORKSHEET • Complete locally, assign an owner and update as planning progresses.

Role	Number	Shift / time	Coordinator	Brief description	Training needed
Registration desk					
Information point					
Family Cup station support					
Public activity-zone support					
Stage / AV support					
Accessibility support					
Water / refreshment point					
Survey support					
Photography / video support					
Clean-up crew					
Logistics / runner support					
Festival operations team					

A10. Budget and suppliers

HOME & HEART ORGANISER WORKSHEET • Complete locally, assign an owner and update as planning progresses.

Cost area	Estimated budget	Confirmed budget	Supplier / provider	Owner	Status	Notes
Venue						
Permits						
Communication						
Equipment rental						
Transport and logistics						
Technical equipment and sport materials						
AV / sound						
Medical / first aid						
Branding / print						
T-shirts / medals / participant materials						
Catering / water						
Photography / video						
Staff / subcontracting						
Volunteer costs						
Accessibility measures						
Waste / sustainability measures						
Travel / accommodation if applicable						
Contingency						

A11. Sustainability and inclusion

HOME & HEART ORGANISER WORKSHEET • Complete locally, assign an owner and update as planning progresses.

Checklist	Measure	Planned?	Owner	Notes
Inclusion	Barrier-free access to venue			
Inclusion	Accessible sanitary facilities			
Inclusion	Inclusive communication materials			
Inclusion	Child-friendly setup			
Inclusion	Support for vulnerable / harder-to-reach families			
Inclusion	Multilingual communication if needed			
Inclusion	Safe participation for different ability levels			
Sustainability	Avoid unnecessary single-use plastics			
Sustainability	Recycling bins and sorting			
Sustainability	Reusable materials			
Sustainability	Sustainable transport messaging			
Sustainability	Low-print / digital-first communication			
Sustainability	Protection of green areas / venue environment			
Sustainability	Waste collection and clean-up plan			

A12. Data collection and reporting

HOME & HEART ORGANISER WORKSHEET • Complete locally, assign an owner and update as planning progresses.

Reporting item	Required?	Owner	Deadline	Format / tool	Notes
Number of registered families					
Number of registered participants					
Number of actual families / participants					
Number of children / adults where reportable					
Number of international Family Cup teams					
Public activity-card participation data					
Family Cup station results and standings					
Number of volunteers / staff					
Participant survey data					
Photos					
Video outputs / livestream					
Media coverage					
Digital / website engagement					
Budget actuals					
Lessons learned					
Incident / risk log					
Follow-up / replication actions					

A13. Risks and mitigation

HOME & HEART ORGANISER WORKSHEET • Complete locally, assign an owner and update as planning progresses.

Risk	Likelihood	Impact	Owner	Mitigation action	Contingency plan
Low registrations					
Severe weather					
Permit delays					
Volunteer shortage					
Supplier cancellation					
Medical incident					
Activity / venue safety issue					
Low survey response					
Branding / materials delay					
Registration or results-system failure					
Livestream / AV failure					
Accessibility issue					
Budget overrun					
Other					

A14. Lessons learned and recommendations

HOME & HEART ORGANISER WORKSHEET • Complete locally, assign an owner and update as planning progresses.

Reflection area	Notes
What worked well	
What should be improved next time	
Most important operational lesson	
Participant feedback themes	
Partner / federation feedback	
Volunteer / staff feedback	
Safety / risk lessons	
Communication lessons	
Recommended changes for next edition	
Recommendations for other organisations replicating Home & Heart	

The long-term value of Home & Heart lies in making family sport participation easier to repeat. Organisers are encouraged to retain the checklists, station instructions, communication assets, results methods and lessons learned so that each new edition can start from a stronger base rather than from zero.



Home & Heart - movement, cooperation and shared family experiences.

Digital legacy

All project materials and future resources can be made accessible through the Home & Heart Digital Knowledge Hub: familyactivityhub.com.



Co-funded by
the European Union
